Nordstrom Contracting
Consulting Corp
36 Theills Mt Ivy Rd
Pomona, NY 10970

LETTER OF TRANSMITTAL

Project: 561A4-13-110
Lyons Porches & Roofs
04/12/2019

To: Gary Boehner

General Engineer
Lyons Campus
151 Knollcroft Rd
Lyons, NJ 07939

Submittal # 2

We are sending you [ ] Herewith [ ] Delivered by Hand [ ] Under Separate Cover [X] Via **ELECTRONIC**

[ ] Plans [ ] Prints [ ] Shop Dwgs [ ] Samples [ ] Specifications [X] Other _____

Copies	Item	# Pages	Description
1	1	1	Initial Schedule

The Above Listed Items are transmitted as indicted below:

Return By Date: SEE BAR CHART

[ ] Approval [ ] As Requested [ ] For Your Use [ ] For Construction

[ ] [ ] Approved As Noted [ ] Submit _____ Copies for Record Distribution

[ ] Returned for Correction, Revise & Resubmit [ ] Coordination (Should the attached be in conflict with your work, advise immediately)

[ ] For Your Files [ ] Other: _____

[ ] For Bids Due _____

Remarks: _____

Project: 561A4-13-110- Lyons- Porch & Roof Renovations- Buildings 10 & 11

Nordstrom Contracting & Consulting Corp

Project Start Date: 3/28/2019 (Thursday)

Project end date: 3/27/2020 (Friday)
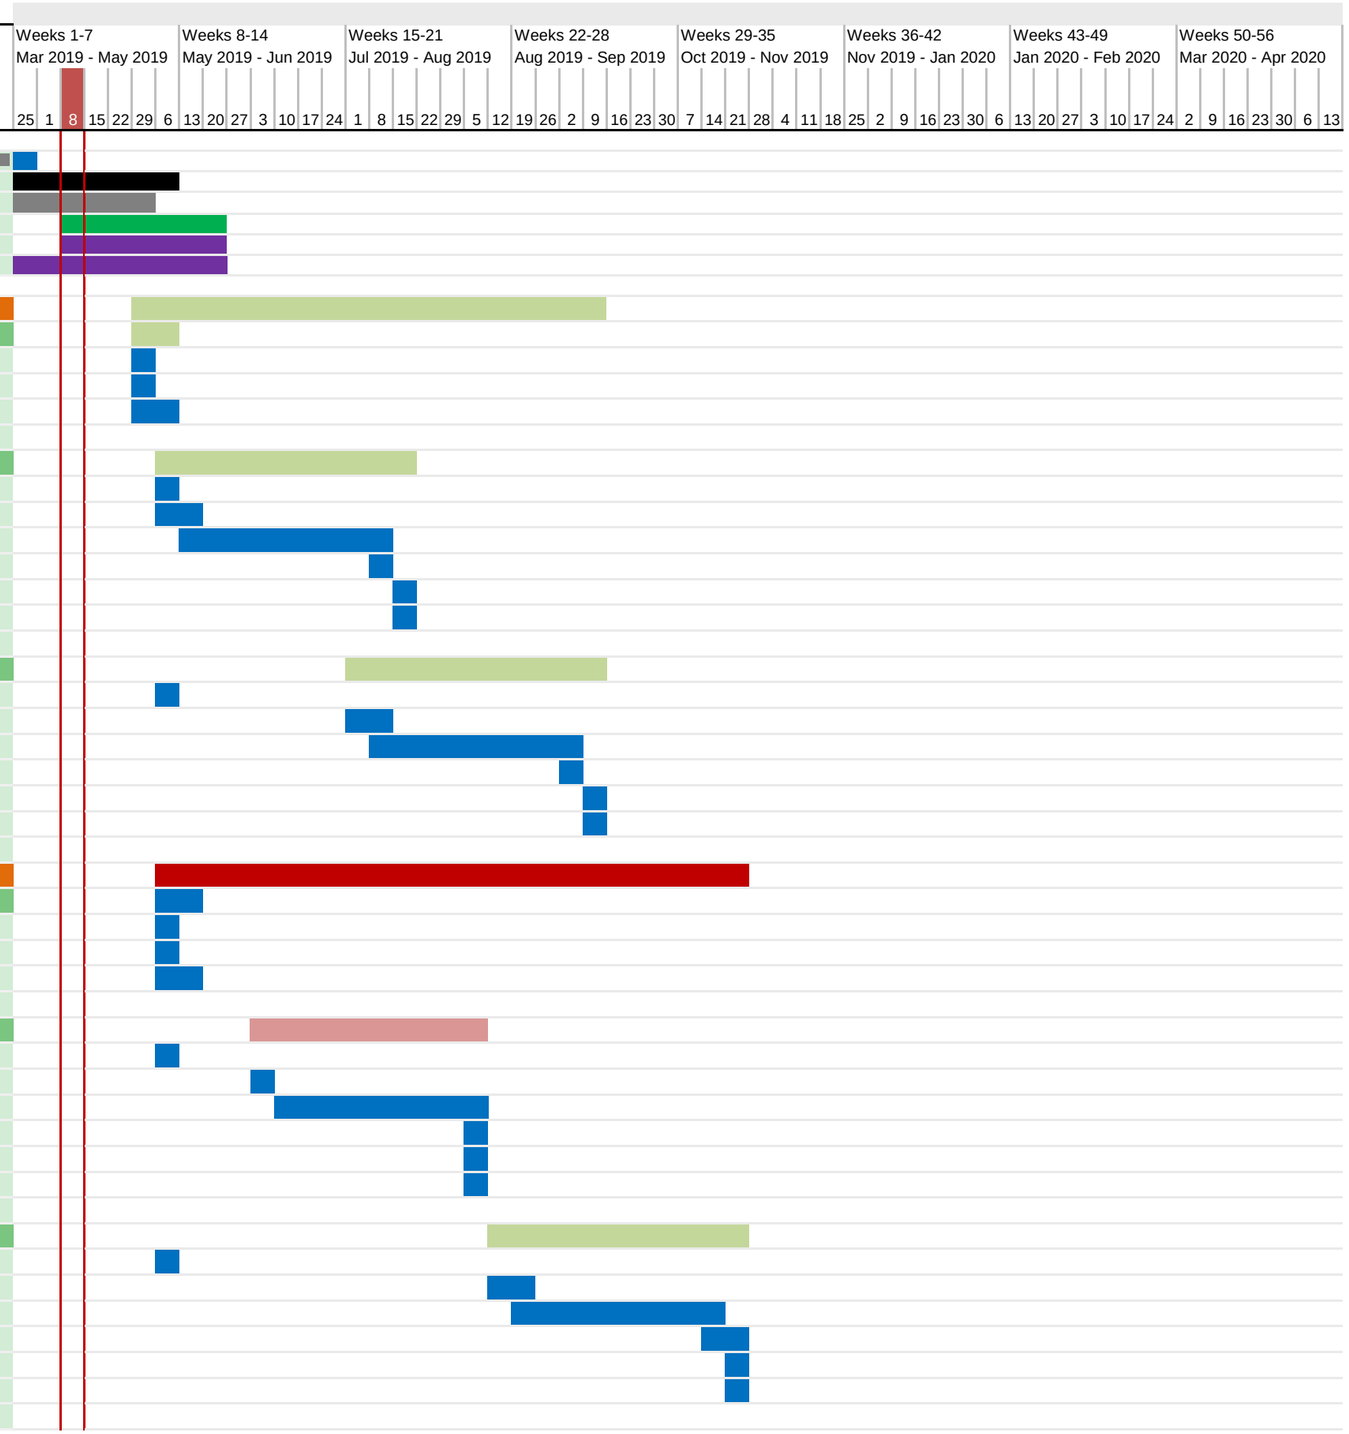
Item	Task	Start	End	Work Days	Cal. Days	% Done
1	**Critical Submittals**					
1.1	Notice To Proceed	Thu 3/28/19	Thu 3/28/19	1	1	100%
1.2	Critical Submittals	Fri 3/29/19	Fri 5/10/19	30	43	25%
1.3	Asbestos Abatement Submittals	Fri 3/29/19	Mon 4/29/19	21	32	10%
1.4	Section Submittals	Mon 4/08/19	Mon 5/20/19	30	43	10%
1.5	Schedule	Mon 4/08/19	Mon 5/20/19	30	43	10%
1.6	Mobilization	Thu 3/28/19	Mon 5/20/19	10	54	10%
	BUILDING 11	Mon 4/29/19	Tue 9/10/19		135	0%
	MAIN ROOF	Mon 4/29/19	Mon 5/06/19		8	0%
0.1	DEMO EXISTING ROOFING- TEMP PROTECTION	Mon 4/29/19	Tue 4/30/19	2		
0.2	NEW ROOFING	Tue 4/30/19	Fri 5/03/19	4		
0.3	PUNCH LIST	Fri 5/03/19	Mon 5/06/19	2		
	BUILDING 11- PORCH 1 (NORTH)	Tue 5/07/19	Tue 7/16/19		71	0%
	ASBESTOS ABATMENT	Tue 5/07/19	Tue 5/07/19	1		
	PORCH DEMOLITION	Wed 5/08/19	Mon 5/13/19	4		
	REBUILD	Tue 5/14/19	Wed 7/10/19	40		
	PORCH ROOFING	Thu 7/11/19	Fri 7/12/19	2		
	PORCH FINISHES / RAILINGS, ETC.	Mon 7/15/19	Mon 7/15/19	0		
	PUNCH LIST	Tue 7/16/19	Tue 7/16/19	0		
	BUILDING 11- PORCH 2 (SOUTH)	Mon 7/01/19	Tue 9/10/19		72	0%
	ASBESTOS ABATMENT	Wed 5/08/19	Wed 5/08/19	1		
	PORCH DEMOLITION	Tue 7/02/19	Mon 7/08/19	4		
	REBUILD	Tue 7/09/19	Wed 9/04/19	40		
	PORCH ROOFING	Thu 9/05/19	Fri 9/06/19	2		
	PORCH FINISHES / RAILINGS, ETC.	Mon 9/09/19	Mon 9/09/19	0		
	PUNCH LIST	Tue 9/10/19	Tue 9/10/19	0		
2	**BUILDING 10**	Mon 5/06/19	Tue 10/22/19		170	0%
2.1	**MAIN ROOF**	Mon 5/06/19	Mon 5/13/19	7	8	0%
2.2	DEMO EXISTING ROOFING- TEMP PROTECTION	Mon 5/06/19	Tue 5/07/19	2		
2.3	NEW ROOFING	Tue 5/07/19	Fri 5/10/19	4		
2.4	PUNCH LIST	Fri 5/10/19	Mon 5/13/19	2		
0.1	**BUILDING 10- PORCH 1 (EAST)**	Mon 6/03/19	Fri 8/09/19	67	68	0%
0.2	ASBESTOS ABATMENT	Thu 5/09/19	Thu 5/09/19	1		
0.3	PORCH DEMOLITION	Tue 6/04/19	Fri 6/07/19	4		
0.4	REBUILD	Mon 6/10/19	Mon 8/05/19	40		
0.5	PORCH ROOFING	Tue 8/06/19	Wed 8/07/19	2		
	PORCH FINISHES / RAILINGS, ETC.	Thu 8/08/19	Thu 8/08/19	0		
0.1	PUNCH LIST	Fri 8/09/19	Fri 8/09/19	0		
0.1	**BUILDING 10- PORCH 2 (WEST)**	Tue 8/13/19	Tue 10/22/19	70	71	0%
0.2	ASBESTOS ABATMENT	Fri 5/10/19	Fri 5/10/19	1		
0.3	PORCH DEMOLITION	Wed 8/14/19	Mon 8/19/19	4		
0.4	REBUILD	Tue 8/20/19	Thu 10/17/19	40		
0.5	PORCH ROOFING	Fri 10/18/19	Mon 10/21/19	2		
	PORCH FINISHES / RAILINGS, ETC.	Tue 10/22/19	Tue 10/22/19	0		
0.1	PUNCH LIST	Tue 10/22/19	Tue 10/22/19	0
