Project: 620-14-114 - Bld 29 Montrose Roof Replacement

Nordstrom Contracting & Consulting Corp

Project Start Date: 1/13/2022 (Thursday)

Project end date: 1/13/2023 (Friday)

Nordstrom Contracting Consulting Corp

Project 620-14-114
Bld 29 Roof Replacement
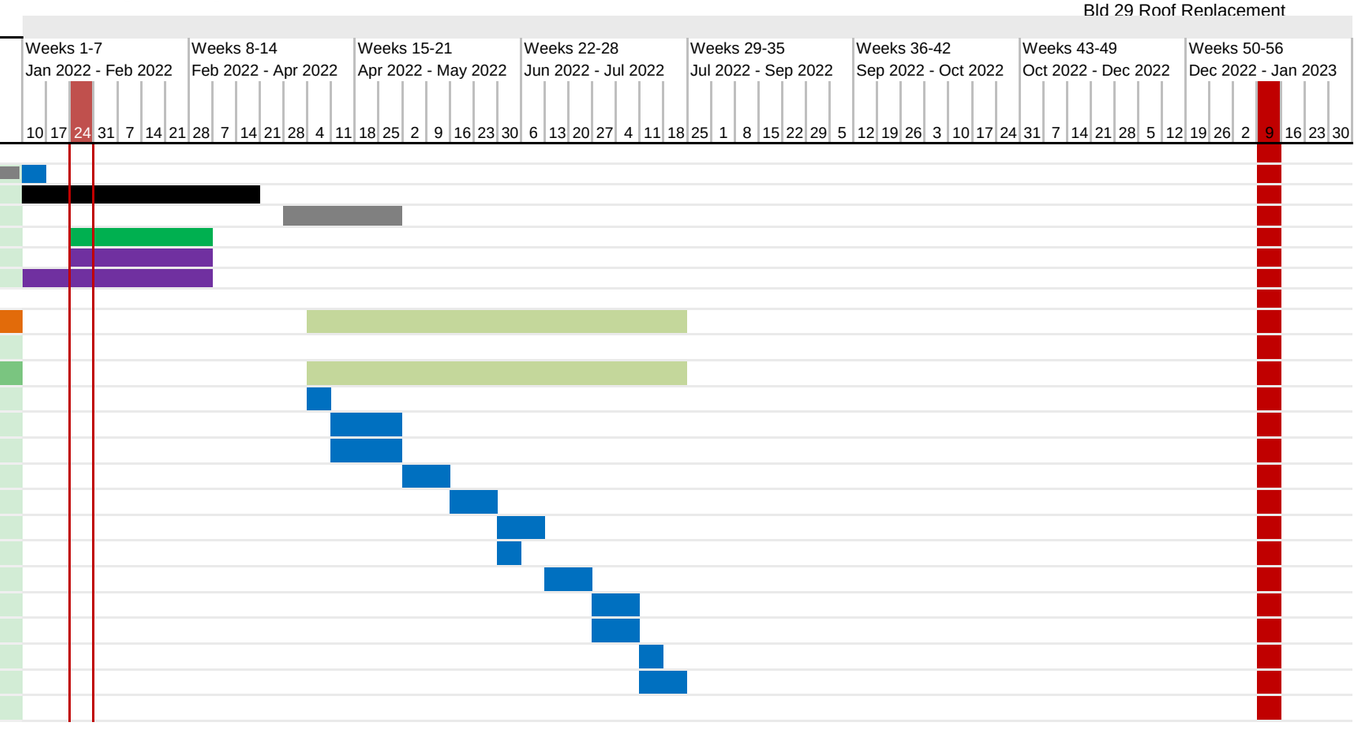
Item	Task	Start	End	Work Days	Cal. Days	% Done
1	**Critical Submittals**					
1.1	Notice To Proceed	Thu 1/13/22	Thu 1/13/22	1	1	100%
1.2	Critical Submittals	Fri 1/14/22	Thu 3/17/22	45	63	25%
1.3	Asbestos Abatement Submittals	Fri 4/01/22	Fri 4/29/22	21	29	10%
1.4	Section Submittals	Mon 1/24/22	Fri 3/04/22	30	40	10%
1.5	Schedule	Mon 1/24/22	Fri 3/04/22	30	40	10%
1.6	Mobilization	Thu 1/13/22	Fri 3/04/22	10	51	10%
	BUILDING 11	Mon 4/04/22	Tue 7/19/22		107	0%
	Building 29- Roof Work	Mon 4/04/22	Tue 7/19/22	106	107	0%
	Instllation of scaffolding @ entrances	Mon 4/04/22	Fri 4/08/22	5	5	
	ASBESTOS ABATMENT	Mon 4/11/22	Fri 4/29/22	15	19	
	Re-Roofing	Mon 4/11/22	Fri 4/29/22	15	19	
	Installation of fall protection	Mon 5/02/22	Fri 5/13/22	10	12	
	Gutter work- Attick Gable work & vents	Mon 5/16/22	Fri 5/27/22	10	12	
	Lightning Protection	Mon 5/30/22	Fri 6/10/22	10	12	
	Building exterior restorations	Mon 5/30/22	Fri 6/03/22	5	5	
	Replace platform & stairs at rear entrance	Mon 6/13/22	Fri 6/24/22	10	12	
	Lightning Protection	Mon 6/27/22	Fri 7/08/22	10	12	
	Gutter downsprout work	Mon 6/27/22	Fri 7/08/22	10	12	
	Restoration of landscaping	Mon 7/11/22	Tue 7/12/22	2	2	
	PUNCH LIST	Wed 7/13/22	Tue 7/19/22	5	7
